Project Plan

Time Management Web App

Primary Instructor	Anjana Shah
Team Member	Sokmontrey Sythat
Team Member	Samuel Browne
Team Member	Jonathan Cao
Team Member	—

Document Revision History

Revision #	Date
1	02/06/2026

Table of Contents

1. Executive Summary

2. Project Approvers, Reviews and Distribution List

3. Scope

4. Deliverables

5. Assumptions

6. Dependencies

7. Risk Management

8. Communication

9. Task Listing (WBS- Work Breakdown Structure)

10. Gantt Chart

11. Milestones

12. RAM – Responsibility Assignment Matrix

13. Approval

1. Executive Summary

The following describes the project to be executed.

Objective	- Develop a web application with efficient user interface - Provide time management, priority recommendation, and task allocation features - Facilitate schedule sharing and synchronize workspace between users within constrained resources (time and budget)
Corporate Goals Addressed	- Improve productivity of individuals with a time management system focused on effective, non-blockage UI. - Connect collaborators across the industry to a single time management solution.
Planned Start Date	September 15th, 2025
Planned End Date	March 27th, 2026

2. Project Approvers, Reviews and Distribution List

Approvers, reviewers and distribution list

Project Role	Name	E-mail	Date
Project Manager	Sokmontrey Sythat	sokmontrey.sythat@georgebrown.ca	01/10/2025
Consultant	Anjana Shah	ashah@georgebrown.ca	01/10/2025
----------	----------	----------	----------
UI/UX	Jonathan Cao	jonathan.cao@georgebrown.ca	01/10/2025
Quality Assurance Engineer	Samuel Browne	samuel.browne@georgebrown.ca	01/10/2025

3. Scope

Define the sum total of all of its products and their requirements or features.

In Scope	Out of Scope
Web platform	Natural language base interface
Share feature	Mobile platform
Common availability finder	
Time recommendation	

4. Deliverables

This project will deliver the following.

Deliverable	Description
Web platform	A web app where the user can use our app. The app will have have calendar interface
Share feature	This will allow the user to share their calendar as well as use our app to find a time that works for both users
Common availability finder	This feature will allow the user to find a common time(time where both users are available) and then let the user block that time off.
Time recommendation	This feature will recommend a time when the user is making a new event

5. Assumptions

This project makes the following assumptions;

- Users are seeking new time management system
- Users are facing blockage with their current time management solution due to ineffective user interface.
- Users require collaborative features such as schedule sharing, common time finder, and real-time collaboration.

6. Dependencies

The following are the internal and external dependencies that will have to be acknowledged and addressed;

1. Team availability: each team member must complete a consistent amount of hours per week throughout the planning/development phase

2. Database and server: server hosting and data storage service is required for certain features of the platform and to ensure that it is widely accessible from most of our users.
3. Task sequencing: development requires successful completion of all tasks during and after the planning phase.
4. Third party software library and framework: development requires stable, opensource, and secure third party solutions for the implementation of specific features.
5. Development environment and software license: integrated development environment and development tools may require subscription.

7. Risk Management

Potential Risk	Severity (H/M/L)	Likelihood (H/M/L)	Management Strategy
Estimate project timeline	L	M	Understand the high-level view of the project to estimate development time
Front-end and Back-end integration	H	M	Design a comprehensive system architecture that includes every aspect of the software.
Challenging UI development	H	M	Development of a comprehensive mockup and UI/UX design before the start of the technical development.
Software error and issues	H	M	Following software development best practices and focusing on implementing application testing ranging from unit to integration testing.
Competition from existing platforms	L	H	Difference the app by focusing on collaborative feature and improving user experience

8. Communication

Reporting

The following reports will be produced;

Report	Audience	Frequency
Sprint minutes	Stakeholders and Consultants	Bi-Weekly
Project statement	Stakeholders and Consultants	Once

User Stories	Stakeholders and Consultants	Once
Team Charter	Stakeholders and Consultants	Once
Project Plan	Stakeholders and Consultants	Quarterly
Product Backlog	Stakeholders and Consultants	Monthly
Sprint Backlog	Stakeholders and Consultants	Monthly
System Requirements	Stakeholders and Consultants	Quarterly
System Design	Stakeholders and Consultants	Quarterly
Wireframes	Stakeholders and Consultants	Once
Technical Requirements	Stakeholders and Consultants	Bi-Annually

Meetings

The following meetings/communication will be established;

Meeting	Purpose	Attendees	Frequency
Standup meeting	- explain project progress - plan upcoming deliverables - assign task to team members	All of the team	weekly
Team meeting/parallel working	Collaborate on current feature and helping each other	Team members that are free to work together	As needed

9. Task Listing (WBS- Work Breakdown Structure)

The following resource proposal template summarizes the resource hours committed to this project, upon final approval of this document.

Reference	Tasks	Duration	Dependency
A	Project Vision, Business Requirements,	2 WEEKS	-

	Personas, User Stories.		
B	Project Plan, Team Charter, Scope, Duration.	2 WEEKS	A
C	System Requirements, Analysis & Design Portfolio.	2 WEEKS	B
D	Wireframes, Prototype, Technical Requirements.	3 WEEKS	C
E	Presentations & Final Report (Oct–Dec).	2 WEEKS	A-B

10. Gantt Chart

Create a detailed Gantt Chart from your Task Listing(Use any software tool and paste the image or upload as a separate file that can be opened as pdf/doc/xls)

Below is an example:

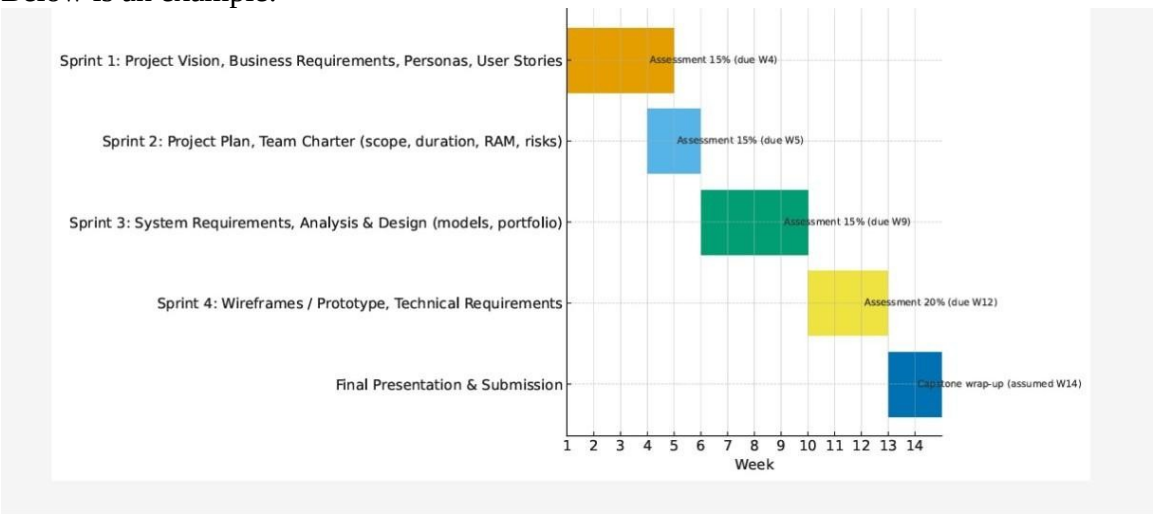

11. Milestones

Major Activity or Milestone	Estimated Milestone Target date	Owner/Reviewer Team Members
Project Vision, Business Requirements, Personas, User Stories.	**Week 4**	Sokmontrey — Samuel Jonathan
Project Plan & Team Charter.	**Week 6**	— Sokmontrey Samuel

		Jonathan
System Requirements, Analysis & Design portfolio.	**Week 9**	— Sokmontrey Samuel Jonathan
Wireframes/Prototype, Technical Requirements.	**Week 12**	Jonathan — Samuel Sokmontrey

12. RAM – Responsibility Assignment Matrix

Create a RAM from your Task Listing. A sample is shown below:

Tasks	Sokmontrey	Jonathan	Samuel	—
Project Timeline Management	P	S	S	—
Design Software Architecture	P	S	S	—
Low-level architecture (code design)	P	S	P	—
Design UI/UX mockup	S	P	S	—
QA/Testing	S	S	P	—

P = Primary S= Secondary

13. Approval

The signatures below indicate their approval of the contents of this document.

Project Role	Name	Signature	Date
Project Manager	Sokmontrey Sythat	S.S	02/06/2026
UI/UX	Jonathan Cao	J.C	02/06/2026
Quality Assurance Engineer	Samuel Browne	S.B	02/06/2026
Software Architect	All	N/A	02/06/2026
